




CAPITAL PROJECTS OVERVIEW

2025 Capital Project Expenditure Summary

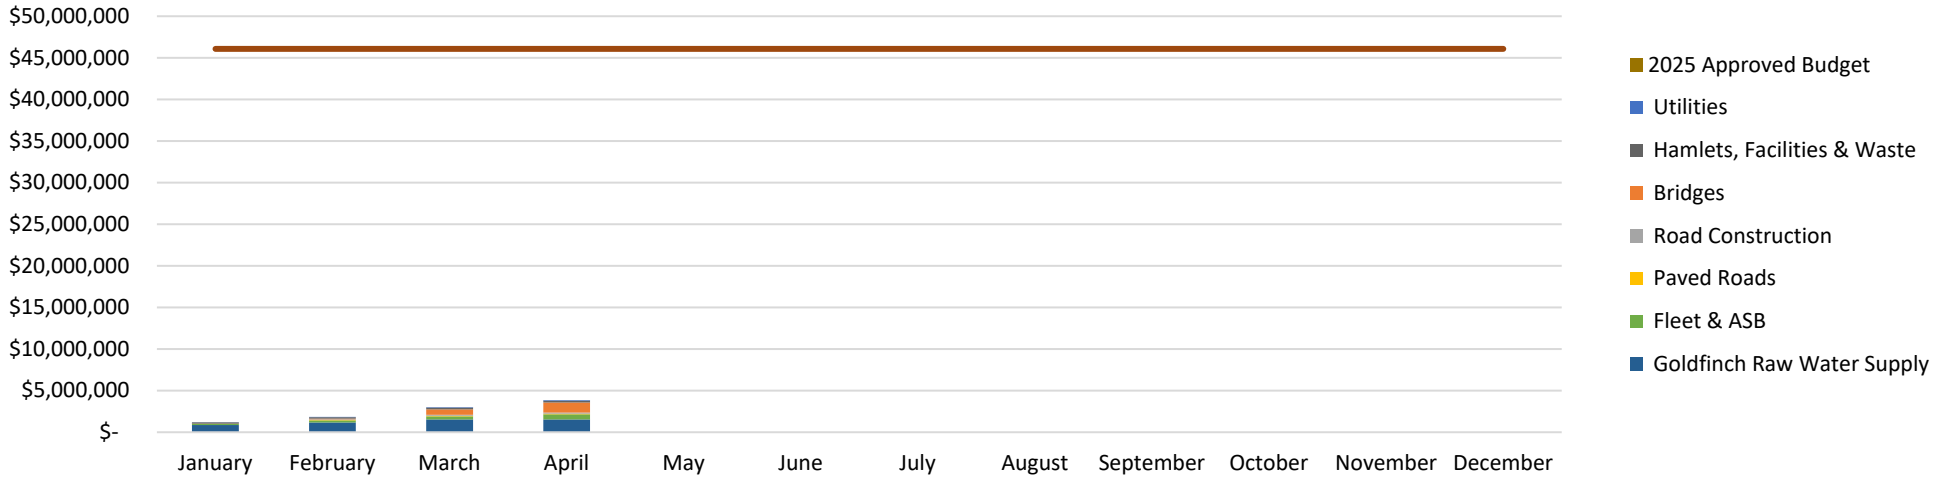

2025 Capital Project Budgets and Expenditure Summary

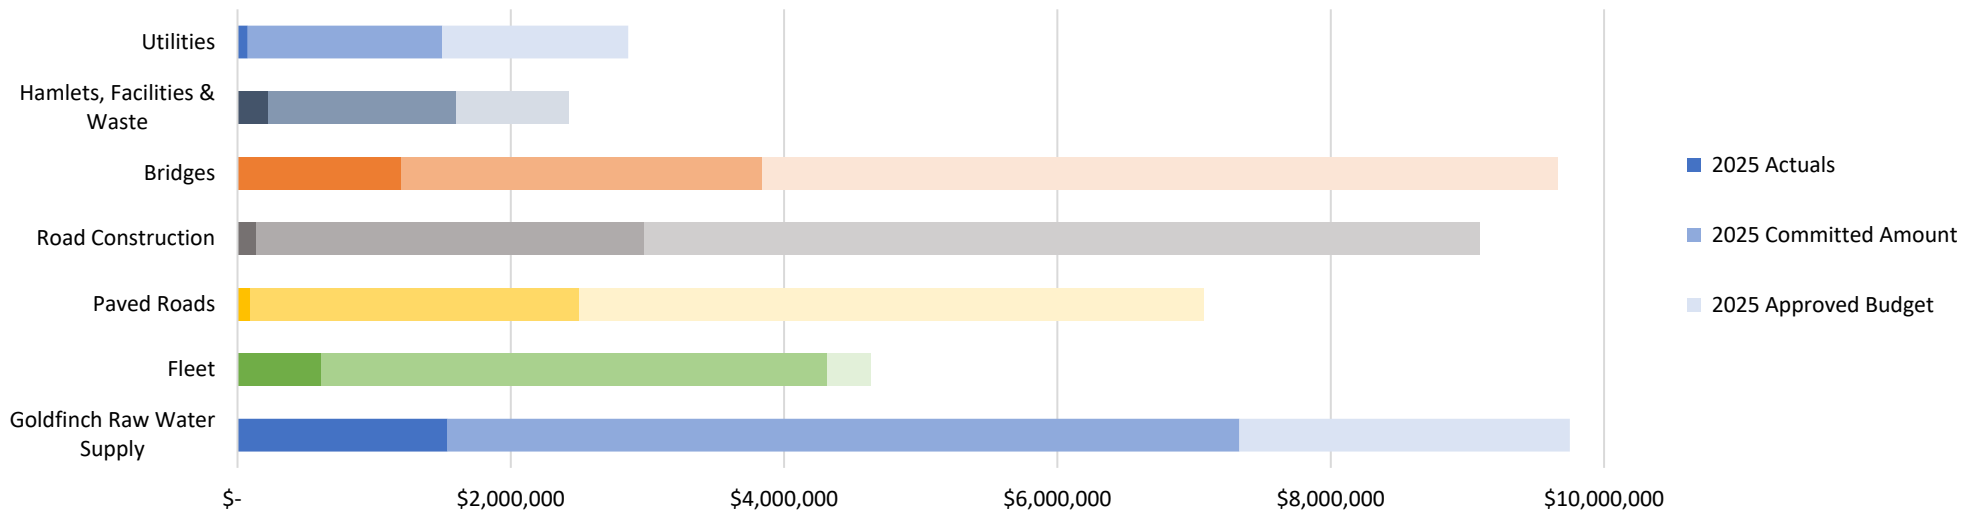


TABLE 1: CAPITAL PROJECTS

PROJECT	DIVISION	LOCATION	CURRENT YEAR PROGRESS	Engineering: Surveyed							Engineering: Prelim.	Engineering: Detailed	Landowners: Detailed	Construction: Approved	Construction: Started	Close out: Finished	Close out: Completed	NOTES
				X	X	X	X	X	X	X								
PUBLIC WORKS - HAMLETS - 31-00																		
HAMLET SIDEWALKS/CONCRETE	2	GLEICHEN/ CLUNY	30%	X	X	X	NA											-Project out for tender, closes May 1, 2025
PUBLIC WORKS - BRIDGES - 32-07																		
BF 73714 - (SW-33-22-25-4)	3	RR254 between HWY901 - TWP230	10%	X	X	X	X	X	X									-Fence adjustments have been completed and deficiency repairs and seeding are to occur in the coming weeks.
BF 70627 - (SW-32-22-25-4)	3	RR255 between HWY901 - TWP230	25%	X	X													-Detailed design is being finalized and IOP's are being drafted.
ATUSIS CREEK REALIGNMENT (SW-32-27-22-4)	6	RR225 between TWP280 - TWP274	10%	X														Prelim design is in progress. Survey completed.
BF 13558 (SE-29-23-22-4)	1	TWP234 between RR224 - RR225	0%	X	X	X	X	X	X									-Final fencing in summer.
BF 71954 - (SW-3-28-23-4)	6	RR233 between TWP280 - HWY9	0%	X	X	X	X	X	X									-Final fencing in summer.
TWP 270 PIPE BORE (NW-35-26-21-4)	7	TWP270 between RR211 - RR212	10%	X	X	X	X											-This project has been completed with no noted deficiencies.
BF 74867 - (SW-15-25-22-4)	2	RR223 between TWP252 - TWP254	0%	X	X	X	X	X	X									-Deficiency repairs and seeding in Spring.
BF 70507 - (SE-24-23-22-4)	1	RR220 between TWP232A - TWP234	10%	X	X													-Scheduled to be posted to APC April 23
BF 79522 - (NW-26-22-26-4)	3	RR262 between HWY901 - TWP224	95%	X	X	X	X	X	X									-Road open, deficiencies in spring
BF 08638 - (SW-18-25-24-4)	5	RR250 between TWP252 - HWY564	95%	X	X	X	X	X	X									-Seeding (2025)/ fencing (2026) outstanding
BF 13701 (SW-26-23-22-4)	1	TWP234 between RR221 - RR222	5%	X														-Prelim design is in progress. Survey completed.
BF 75852 - (SE-29-22-26-4)	3	TWP224 between RR264 - RR265	25%	X	X	X												-Design approved by WID, out for landowner signoff
BF 75851 (SW-17-23-25-4)	4	RR255 between TWP232 - TWP232a	0%															-Prelim report in progress.
BF 74391 - (SW-29-26-23-4)	6	TWP264 between RR240 - RR235	50%	X	X	X	X	X	X									-Fence adjustments completed. Monitoring reestablishment of vegetation. -Final fence 2026.
BF 00467 - (NW-20-25-25-4)	5	RR255 between HWY 564 - TWP252	20%	X	X	X	X											-Awaiting ERA permitting prior to tendering.

Completed in prior budget year
 Completed in current budget year
 To be completed current budget year
 Planned for future budget year

TABLE 1: CAPITAL PROJECTS

PROJECT	DIVISION	LOCATION	CURRENT YEAR PROGRESS	CURRENT YEAR PROGRESS								NOTES	
				Engineering: Surveyed	Engineering: Prelim.	Engineering: Detailed	Landowners: Approved	Construction: Started	Construction: Finished	Close out: Completed			
BF 76863 (NW-29-22-26-4)	3	RR265 between HWY901 - TWP224	0%										-Prelim report in progress '- Preliminary Design Report is currently being reviewed by the County.
BF 07943 (SW-23-26-23-4)	2	RR232 between HWY1 - TWP244	0%										-Prelim report in progress
PUBLIC WORKS - GENERAL CONSTRUCTION & ROAD MAINTENANCE - 32-08													
TWP 230 (FROM RR 194 TO HWY 56)	1	TWP 230	0%	X	X	X	X	X	X				-Deficiency repairs 2025.
TWP 280 (FROM HWY 21 TO RR 244)	6	TWP 280	0%	X	X	X	X	X	X				-Fencing to be completed around the bridge file location summer 2025.
TWP 264 (FROM HWY 56 TO RR 203)	7	TWP 264	0%										-Prelim only in 2025. -Consultant is reviewing the previous design, completing a project summary. '- Landowner notification letter is being sent out to all the landowners
RR 205 (FROM TWP 250 TO HWY 564)	7	RR 205	25%	X	X	X	X	X	X				-Temp fence removals in summer 2025.
RR 244 (FROM TWP 232 TO TWP 233)	2	RR 244	0%	X	X	X	X	X	X				-Temp fence to remain in place until 2026 to allow for re-establishment of vegetation.
TWP 240 (FROM HWY 24 TO RR 270)	4	TWP 240	18%	X	X	X	X						-This project was posted to APC on April 15 with a closing date of May 13.
RR 243A (FROM TWP 232 TO NAMAKA)	2	TWP 243A	15%	X	X	X	X	X	X				-Power poles are being relocated. Deficiency repairs to be completed prior to seeding.
TWP 272 ROSEBUD WEST ACCESS	6	TWP 272	50%	X	X	X	X						-Tender closed under budget, contract awarded. -Construction to be mid-July to end of September 2025
TWP 250 (ALIGNMENT CORRECTION AT RR 214)	1	TWP 250	0%										-Survey has been completed and preliminary design is ongoing.
TWP 215A (FROM RR 260 TO JOHNSON ISLAND GATES)	3	TWP 215A	0%	X	X	X	X	X	X				-Fencing late 2025/2026
RECONSTRUCTION OF TWP 222 (FROM HWY 24 TO RR 262)	3	TWP 222	50%	X	X	X	X						-Tender closed under budget, contract awarded. -Construction to be early June to end of September 2025
RR 220A ALIGNMENT	3	TWP 222	0%	X	X	X		NA	NA				-Land negotiations are in progress.
RIGHT OF WAY ALIGNMENTS	NA	Various	0%										-Budget only utilized as required.
PUBLIC WORKS - PAVED ROADS - 32-10													
TWP 250 - CONSTRUCTION & PAVING (FROM HWY 817 TO RR 264)	5	TWP 250	55%	X	X	X	X	X					- Construction started between RR 264-263, anticipated to be complete late May 2025.
RR 233 CHIP SEAL OVERLAY (HWY 1 TO ROCKYFORD)	2/6	RR 233	0%	X	NA	NA	NA						-Tender closed April 15 qith 4 bids recieved.

X Completed in prior budget year
 X Completed in current budget year
 To be completed current budget year
 Planned for future budget year

TABLE 1: CAPITAL PROJECTS

PROJECT	DIVISION	LOCATION	CURRENT YEAR PROGRESS	CURRENT YEAR PROGRESS							NOTES
				Engineering: Surveyed	Engineering: Prelim.	Engineering: Detailed	Landowners: Approved	Construction: Started	Construction: Finished	Close out: Completed	
TWP 234 - GLENMORE MILL & OVERLAY (FROM HWY 24 TO HWY 817)	4	TWP 234	100%	X	X	X	X	X	X	X	-Project Complete.
RR 255 MRO APPLICATION (FROM HWY 901 TO HWY 24)	3	RR 255	0%	X	NA	NA	NA				-Construction to occur in July with internal forces.
MUIRFIELD - MUIRFIELD BLVD	5	MUIRFIELD	0%	X	X	X	NA				-Contract is with the County for execution. Kick-off meeting and site meeting are being scheduled.
MUIRFIELD - MUIRFIELD CLOSE	5	MUIRFIELD	0%	X	X	X	NA				-Contract is with the County for execution. Kick-off meeting and site meeting are being scheduled.
MUIRFIELD - MUIRFIELD CRESCENT	5	MUIRFIELD	0%	X	X	X	NA				-Contract is with the County for execution. Kick-off meeting and site meeting are being scheduled.
RR 270 RECONSTRUCTION & PAVING (FROM TWP 221 SOUTH)	3	RR 270	10%	X	X						- Surveying and boreholes complete - Traffic study complete, analysis underway
PUBLIC WORKS - FLEET - 33-00											
B-TRAIN BELLY DUMP TRAILERS (2 UNITS)	NA		10%	NA	NA	NA	NA	NA	NA		- Unit ordered.
BOOM MOWER	NA		10%	NA	NA	NA	NA	NA	NA		- Unit ordered.
14' WIDE ANGLE MOWER	NA		100%	NA	NA	NA	NA	NA	NA	X	- Unit delivered.
14M MOTOR GRADERS (2 UNITS)	NA		10%	NA	NA	NA	NA	NA	NA		- Unit ordered.
CLASS 8 HIGHWAY TRACTOR	NA		10%	NA	NA	NA	NA	NA	NA		- Unit ordered.
PICKUPS (3 UNITS)	NA		10%	NA	NA	NA	NA	NA	NA		- Units ordered.
SHOP EQUIPMENT & TOOLS	NA		15%	NA	NA	NA	NA	NA	NA		
CLASS 8 PLOW TRUCK W/ SANDER	NA		10%	NA	NA	NA	NA	NA	NA		- Unit ordered.
PEACE OFFICER VEHICLE (1 UNIT)	NA		10%	NA	NA	NA	NA	NA	NA		- Carry over. Unit is being upfitted.
FLAT DECK TRAILERS (2 UNITS)	NA		50%	NA	NA	NA	NA	NA	NA		- 1 of 2 units delivered.
INTERMODAL CHASSIS	NA		100%	NA	NA	NA	NA	NA	NA	X	
SNOW PUSH	NA		100%	NA	NA	NA	NA	NA	NA	X	
CLASS 7 TRUCK W/ DUMP	NA		10%	NA	NA	NA	NA	NA	NA		- Unit ordered.
UTILITY WORK MACHINE W/ ATTACHMENTS	NA		100%	NA	NA	NA	NA	NA	NA	X	
TRENCH COMPACTOR	NA		100%	NA	NA	NA	NA	NA	NA	X	
DRIVE OVER TRANSFER CONVEYOR	NA		100%	NA	NA	NA	NA	NA	NA	X	
STORM DRAINAGE- 40-00											
CHEADLE - BACKLANE & HALL DRAINAGE	4		0%								-Drawings submitted to the County for Cheadle Hall drainage concerns. Drawings are being reviewed by the County for the Backlanes.
WATER - 41-00											
GOLDFINCH RAW WATER SUPPLY	3	GOLDFINCH	21%	X	X	X	NA	X			-Drilling underway along HWY 24, progressing west.
REDLAND - WATER SERVICING	5	MUIRFIELD	2%	NA	X	X					- County completed drafting Cost Contribution Agreement to each landowner

Completed in prior budget year
 Completed in current budget year
 To be completed current budget year
 Planned for future budget year

TABLE 1: CAPITAL PROJECTS

PROJECT	DIVISION	LOCATION	CURRENT YEAR PROGRESS	CURRENT YEAR PROGRESS								NOTES
				Engineering: Surveyed	Engineering: Prelim.	Engineering: Detailed	Landowners: Approved	Construction: Started	Construction: Finished	Close out: Completed		
WATER MUIRFIELD - 41-11												
MUIRFIELD WTP FENCE	5	MUIRFIELD	0%	X	X	X	NA					Fencing of both entrances at the WTP, summer 2025.
SEWER - 42-00												
GLEICHEN - LIFT STATION REPAIRS	1	GLEICHEN	90%	X	X	X	NA	X				- Electrical revisions and generator installation complete. - Final commissioning late April.
MUIRFIELD - LAGOON	5	MUIRFIELD	2%									Work continues on land negotiations with the one interested landowner.
WASTE MANAGEMENT - 43-00												
LYALTA AREA WASTE TRANSFER SITE	5	Division 5	5%	X	X							-Further site investigation in progress.
WTS OPERATOR SHACK REPLACEMENTS	NA	Various	30%	NA	NA	NA	NA	X				-Electrical outfitting of buildings is underway.
WHEATLAND WEST FENCE REPLACEMENT	4	Wheatland West WTS	0%		NA	NA	NA					-Replacement of north and south fence in summer 2025.
ASB GENERAL - 62-00												
15FT MOWER	NA		100%	NA	NA	NA	NA	NA	NA	X		- Unit delivered.
FACILITIES - 70-00												
PUBLIC WORKS YARD SALT SHED	NA	Public Works Yard	10%	X								-Electrical and Foundation drawings have been reviewed by the County and the mark-ups are with the contractor to address.

Completed in prior budget year

Completed in current budget year

To be completed current budget year

Planned for future budget year
